



Completion Report

conducted for

Domestic customer

Document No.

UIS- 707/22

Job Number

707/22

Location

24 grays Road
Lee
London
SE12

Prepared by

Oliver Judge

Gang Attending

RM01

Operative 2

RM01

Operative 1

RM01

Job Details

Question	Response	Details			
Job Initiation					
Pre-Start photo					
					
Appendix 1	Appendix 2	Appendix 3	Appendix 4	Appendix 5	Appendix 6
					
Appendix 7	Appendix 8	Appendix 9	Appendix 10	Appendix 11	
Job Started					
Health & Safety					
Risk Assessment completed	Yes				
Underground Services Identified	Yes				
Pedestrian Access control	Yes				
Site secured	Yes				
Photo of site					
Works completion					
Works completed	Yes				
Works reinstated	Yes				
Site cleared	Yes				
Description of works undertaken	We attended site to install a new 25MM MDPE water service.				

	<p>We CAT Scanned the proposed working area and set up a safe site.</p> <p>We excavated 2 Moling pits (1m x 0.5m x 0.75m).</p> <p>We installed a new 25 MDPE water service via impact moling.</p> <p>We duct and lagged the pipe as it went through wall of property.</p> <p>We lifted some floorboards and installed the new water service under the floorboards.</p> <p>We made external connections and flushed through the pipework.</p> <p>We made internal connections and tested our installation.</p> <p>We backfilled with as dug material and reinstated to match the existing surfaces.</p> <p>We cleared site.</p>
<p>Please take pictures of each working stage and any relevant additional information (i.e pre start damage etc.).</p>	
<p>Site drawing</p>	
<p>Site Left</p>	
<p>Fittings Used</p>	
<p>Hours Spent</p>	

Materials and Equipment

Question	Response	Details
----------	----------	---------

Media




Appendix 1



Appendix 2




Appendix 3

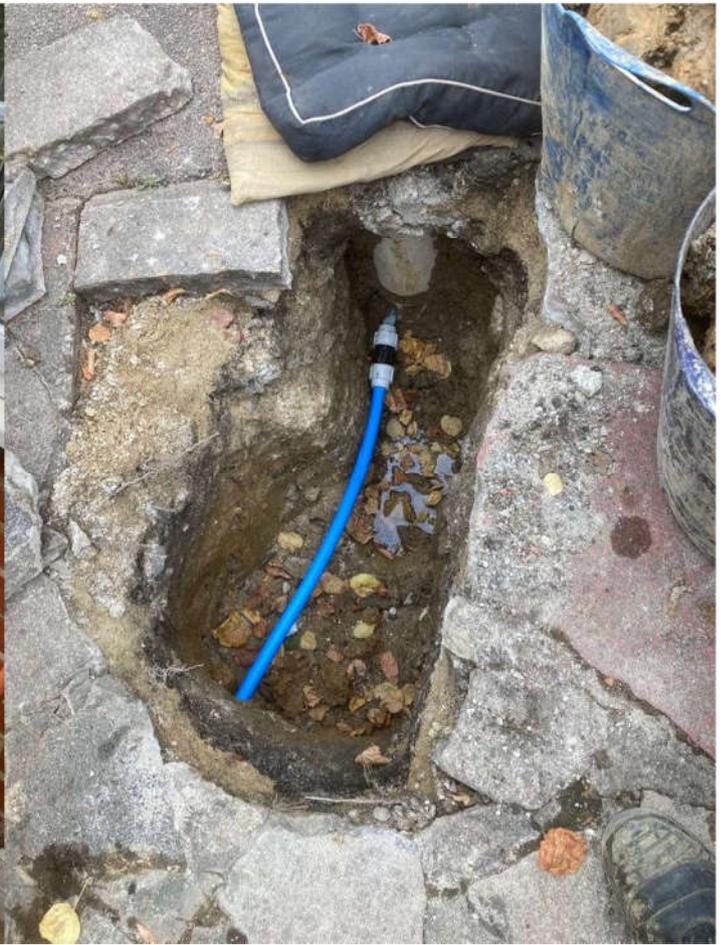

Appendix 4




Appendix 5

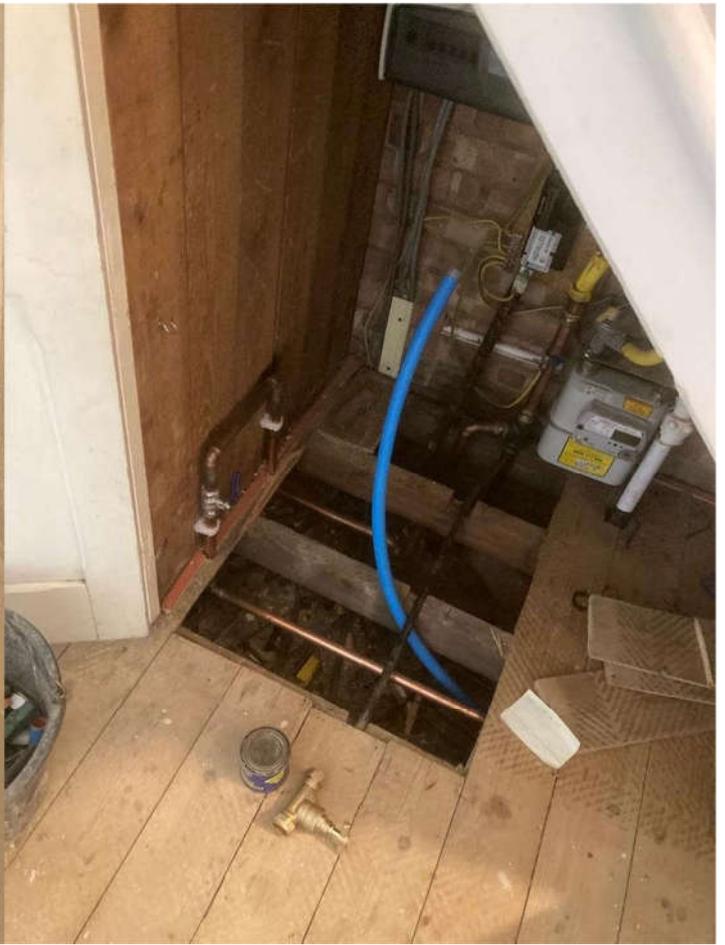


Appendix 6




Appendix 7

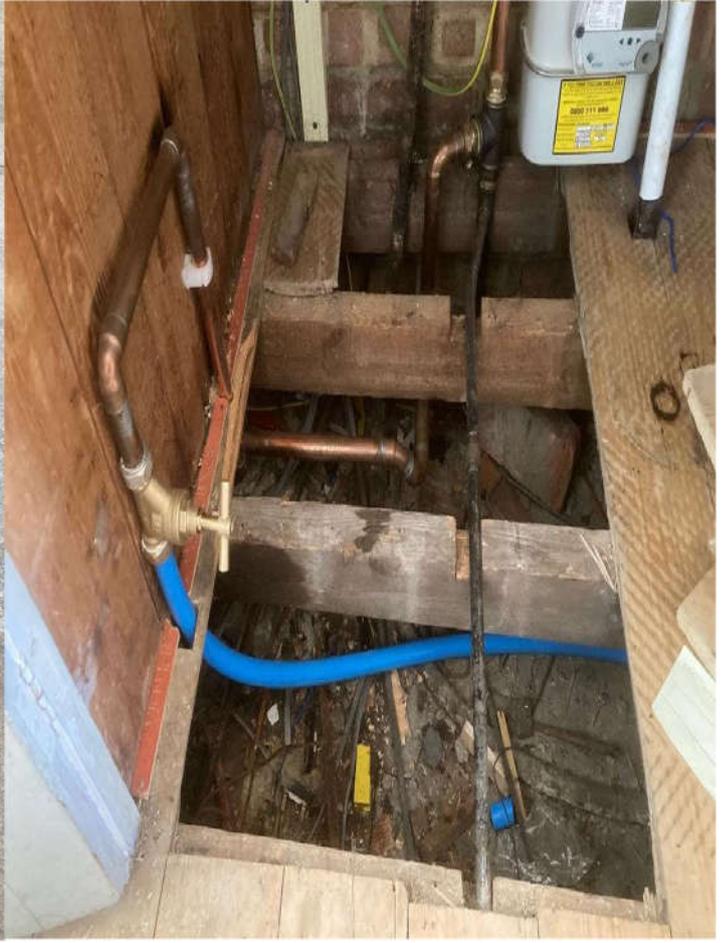

Appendix 8

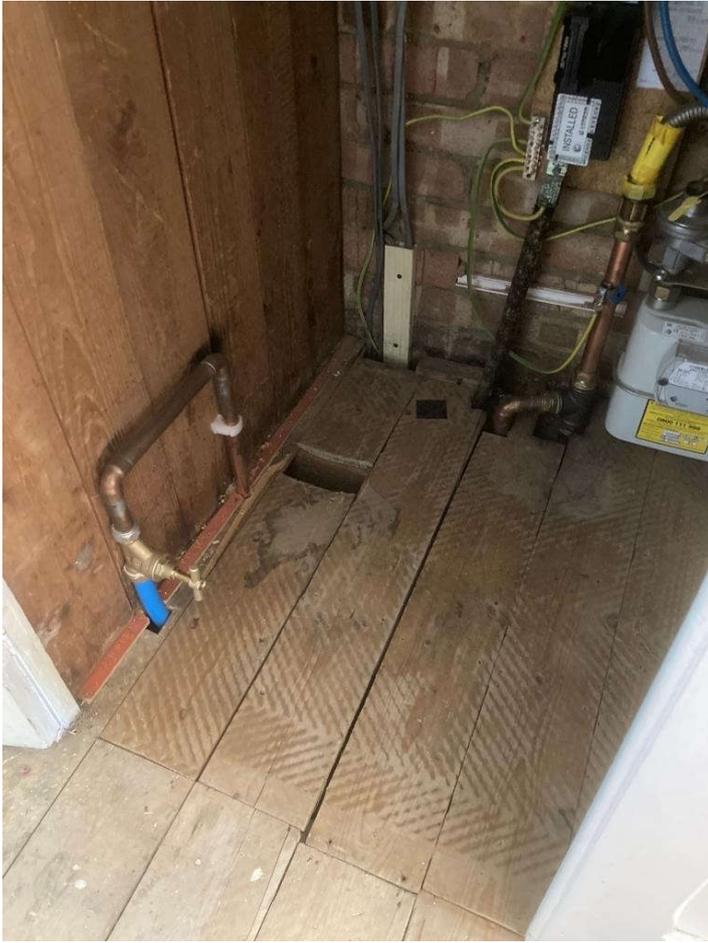

Appendix 9

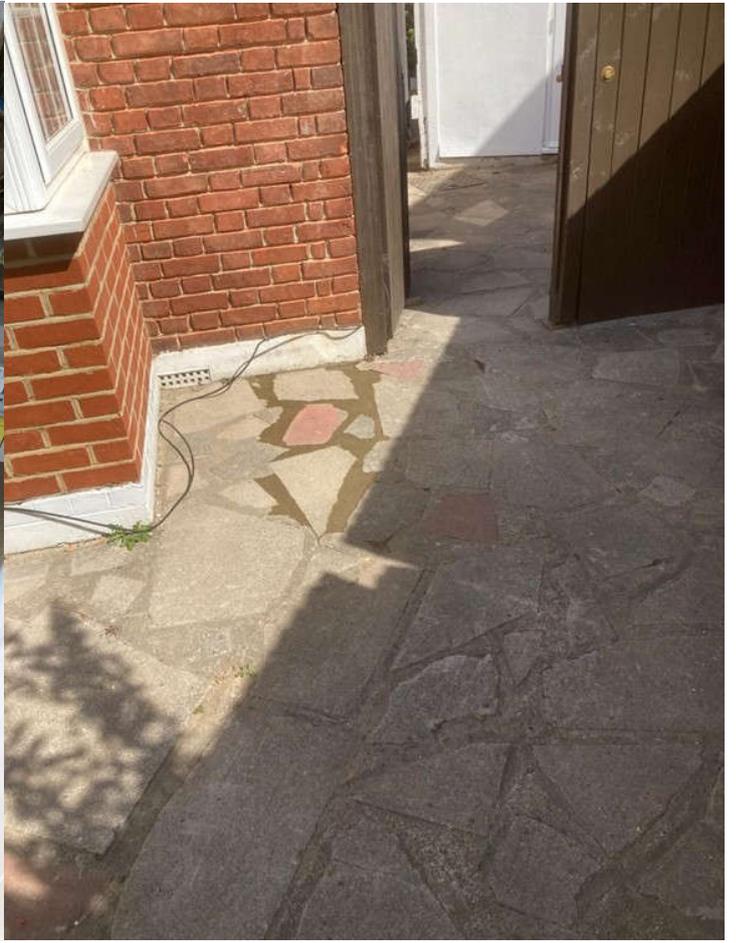

Appendix 10



Appendix 11
